



ID	Task Name	Duration	Start	Finish	h 1	June 11	September 21	January 1	April 11	July 21						
					3/31	5/19	7/7	8/25	10/13	12/1	1/19	3/9	4/27	6/15	8/3	9/21
1	Wolstein Center Family Room Renovation Project	246 days	Fri 2/28/14	Fri 10/31/14												
2	Drawing and Specification Planning	21 days	Fri 2/28/14	Thu 3/20/14												
3	Organizational Meeting	1 day	Fri 3/21/14	Fri 3/21/14												
4	Preliminary Estimate	10 days	Fri 3/21/14	Sun 3/30/14												
5	Interim Funding and Timing	22 days	Mon 3/31/14	Mon 4/21/14												
6	Management Review Decision & Funding	3 days	Mon 3/31/14	Wed 4/2/14												
7	Drawing Preparation	64 days	Fri 2/28/14	Fri 5/2/14												
8	Ziska PO	14 days	Thu 4/3/14	Wed 4/16/14												
9	CD Drawing Preparation & Meetings	14 days	Thu 4/17/14	Wed 4/30/14												
10	CD Drawing Complete	2 days	Thu 5/1/14	Fri 5/2/14												
11	Bidding	66 days	Wed 6/4/14	Fri 8/8/14												
12	Legal Review/Purchasing	48 days	Wed 6/4/14	Mon 7/21/14												
13	Bid week # 001	7 days	Wed 7/23/14	Tue 7/29/14												
14	Bid week # 002	7 days	Tue 7/29/14	Mon 8/4/14												
15	Pre-Bid Meeting	1 day	Tue 7/29/14	Tue 7/29/14												
16	Permitting walk thru & Questions Due	1 day	Wed 7/30/14	Wed 7/30/14												
17	Bid Due	1 day	Thu 8/7/14	Thu 8/7/14												
18	Award Phase	25 days	Fri 8/8/14	Mon 9/1/14												
19	Scope Review	1 day	Fri 8/8/14	Fri 8/8/14												
20	Recommendation of Award	1 day	Mon 8/11/14	Mon 8/11/14												
21	Contract	7 days	Tue 8/12/14	Mon 8/18/14												
22	Contract Submittals	1 day	Thu 8/21/14	Thu 8/21/14												
23	Attorney General	1 day	Mon 8/25/14	Mon 8/25/14												
24	Issue Notice to Proceed	1 day	Mon 9/1/14	Mon 9/1/14												
25	Construction	40 days	Mon 8/25/14	Fri 10/3/14												
26	General Trades	40 days	Mon 8/25/14	Fri 10/3/14												
27	Electrical	8 days	Mon 9/22/14	Mon 9/29/14												
28	Mechanical	7 days	Fri 9/26/14	Thu 10/2/14												
29	Finishes	8 days	Fri 9/26/14	Fri 10/3/14												
30	Inspections	3 days	Mon 10/6/14	Wed 10/8/14												
31	Inspections (All)	1 day	Mon 10/6/14	Mon 10/6/14												
32	Turn over to University	1 day	Wed 10/8/14	Wed 10/8/14												

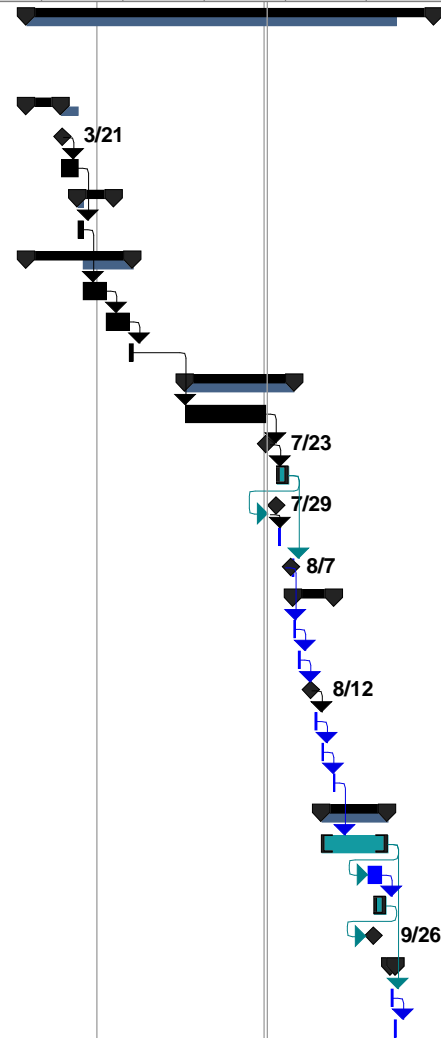

Wolstein Center Family Room Renovation Date: Wed 7/23/14	Task		Project Summary		Manual Summary	
	Milestone		Group By Summary		Start-only	
	Summary		Inactive Task		Finish-only	
	Rolled Up Task		Inactive Milestone		Late	
	Rolled Up Milestone		Inactive Summary		Progress	
	Rolled Up Progress		Manual Task		Deadline	
	Split		Duration-only			
	External Tasks		Manual Summary Rollup			

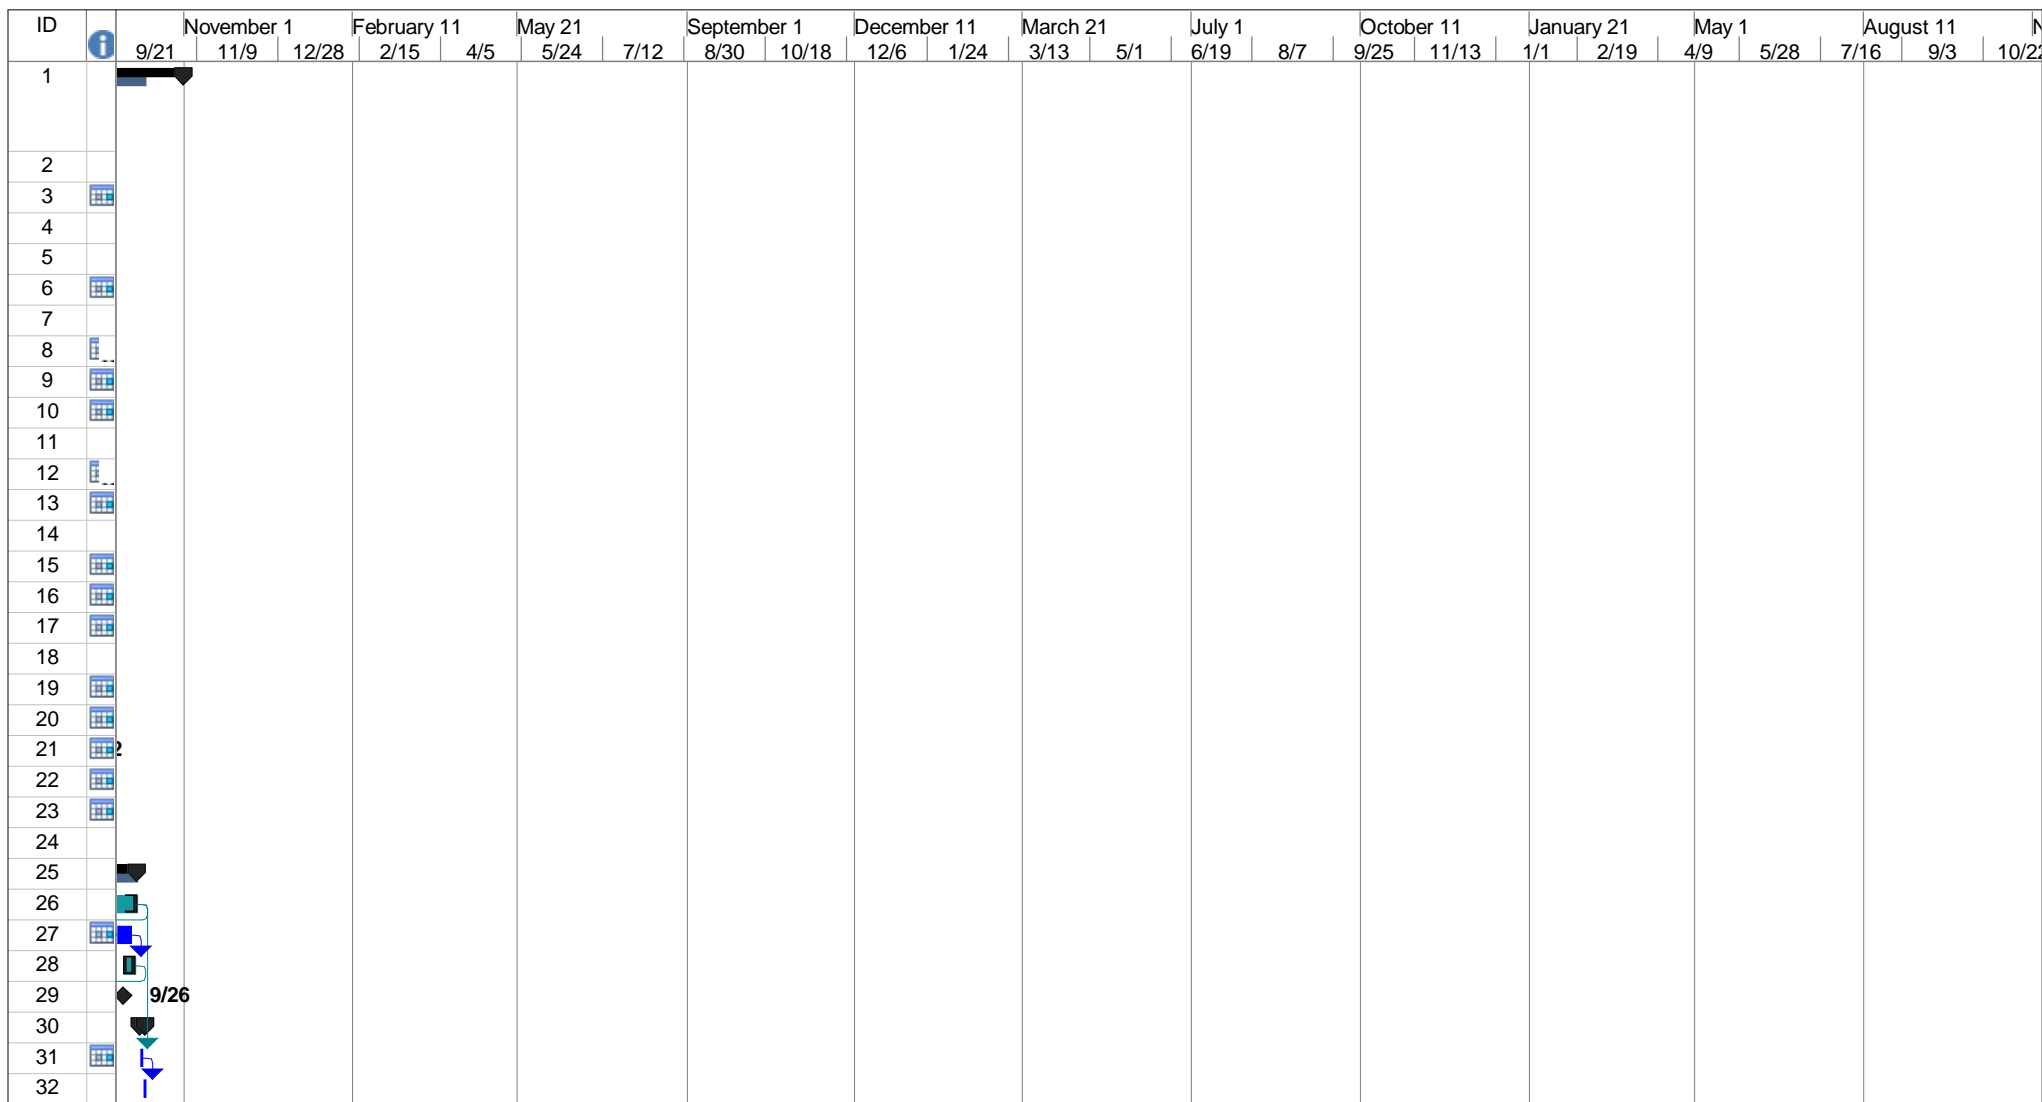

Wolstein Center Family Room Renovatio

Date: Wed 7/23/14

Task		Project Summary		Manual Summary	
Milestone		Group By Summary		Start-only	
Summary		Inactive Task		Finish-only	
Rolled Up Task		Inactive Milestone		Late	
Rolled Up Milestone		Inactive Summary		Progress	
Rolled Up Progress		Manual Task		Deadline	
Split		Duration-only			
External Tasks		Manual Summary Rollup			
