Tue 10/14/14 SH Revised Project Schedule_2013-11-25.mpp

Task Name	ID	Calander Days	No. Months	Start	Finish	% Comple	Status
Fenn Hall	**1**	**0**	**0**	**11/11/13**	**8/18/15**	**28%**	**On Schedule**
A/E - CMR Selection Process	**2**	**0**	**0**	**11/11/13**	**7/15/14**	**100%**	**Complete**
RFQ Preparation	3	12	0.4	11/11/13	11/22/13	100%	Complete
Advertise for A/E	4	38	1.27	11/27/13	1/3/14	100%	Complete
Process A/E Proposals & Select Shortlist	5	22	0.73	1/3/14	1/25/14	100%	Complete
A/E Shortlist Selection Meeting	6	0	0	1/28/14	1/28/14	100%	Complete
Set up A/E Interviews	7	4	0.13	1/28/14	2/1/14	100%	Complete
Board Meeting	8	1	0.03	1/28/14	1/28/14	100%	Complete
CM+Risk RFQ Posted & Advertised	9	1	0.03	1/30/14	1/30/14	100%	Complete
A/E Interviews	10	1	0.03	2/25/14	2/25/14	100%	Complete
A/E Recommend Approval of Selected Firm	11	0	0	2/28/14	2/28/14	100%	Complete
A/E Administration Review	12	43	1.43	2/28/14	4/11/14	100%	Complete
A/E Approval to Select Firm	13	1	0.03	4/22/14	4/22/14	100%	Complete
CM+Risk RFQ Due	14	1	0.03	3/4/14	3/4/14	100%	Complete
A/E Tech Proposal/ Fee Neg	15	31	1.03	5/7/14	6/6/14	100%	Complete
CM+Risk Shortlist - Issue RFP	16	5	0.17	4/7/14	4/11/14	100%	Complete
Board Meeting	17	1	0.03	3/25/14	3/25/14	100%	Complete
CM+Risk Site Visit / Meeting	18	1	0.03	4/21/14	4/21/14	100%	Complete
A/E Contracts Signed	19	12	0.4	6/6/14	6/18/14	100%	Complete
CM+R Proposals Due	20	1	0.03	5/13/14	5/13/14	100%	Complete
A/E Notice to Proceed	21	0	0	7/6/14	7/6/14	100%	Complete
CM+Risk Interviews	22	1	0.03	5/20/14	5/20/14	100%	Complete
CM+Risk Admin Review Period	23	32	1.07	5/20/14	6/20/14	100%	Complete
Board Meeting	24	1	0.03	5/20/14	5/20/14	100%	Complete
CM+Risk Final Selection	25	0	0	5/28/14	5/28/14	100%	Complete
CM+R Fee Negoations	26	14	0.47	6/4/14	6/18/14	100%	Complete
CM+R Contract Prep and Signatures	27	21	0.7	6/24/14	7/15/14	100%	Complete
Planning Study & Programming	**28**	**1**	**0.03**	**7/7/14**	**10/8/14**	**31%**	**Late**
Project Kick-Off Meeting & Introduction CBLH/ I	29	5	0.17	7/7/14	7/11/14	100%	Complete
Engineering Idea Sessions with Designers	30	16	0.53	7/16/14	7/31/14	100%	Complete
Facilities / Architect Review of Systems/Hazard	31	16	0.53	7/16/14	7/31/14	100%	Complete
Core Group Planning Meeting #1	32	1	0.03	8/5/14	8/5/14	100%	Complete
Work Session #1	33	14	0.47	8/6/14	8/19/14	100%	Complete

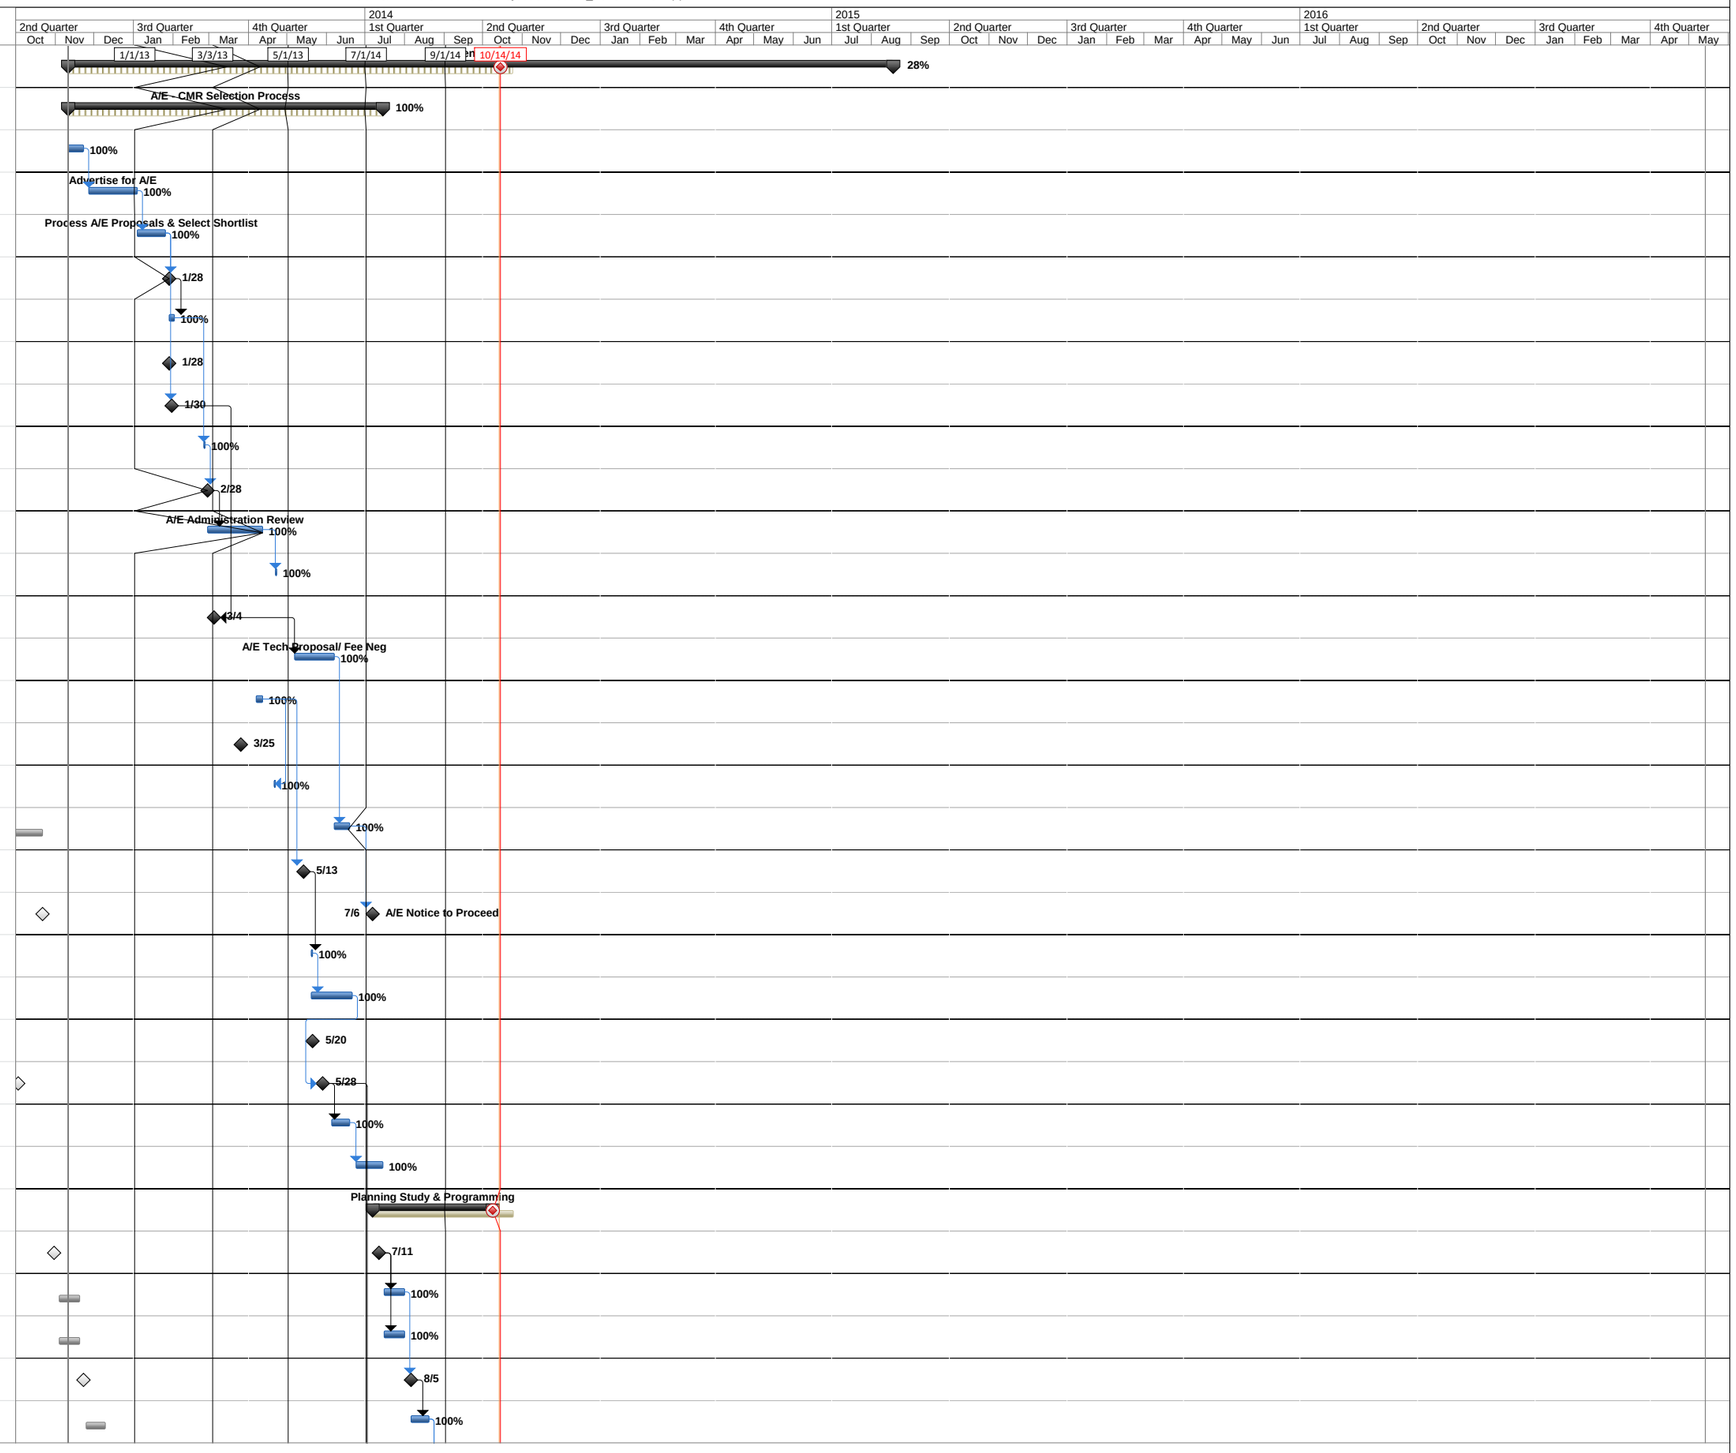

Critical | Task | Manual Task | Duration-only | Baseline Milestone | Summary | External Tasks | Inactive Milestone
Critical Split | Split | Start-only | Baseline | Milestone | Manual Summary | External Milestone | Inactive Summary
Critical Progress | Task Progress | Finish-only | Baseline Split | Summary Progress | Project Summary | Inactive Task | Deadline

Tue 10/14/14 SH Revised Project Schedule_2013-11-25.mpp

Task Name	ID	Calander Days	No. Months	Start	Finish	% Comple	Status
Engineering Retreat / CBLH-HED Presentation	34	1	0.03	8/22/14	8/22/14	100%	Complete
Core Group Planning Meeting #2	35	1	0.03	8/22/14	8/22/14	100%	Complete
Work Session #2	36	13	0.43	8/20/14	9/1/14	100%	Complete
CM+Risk Notice to Proceed	37	1	0.03	7/7/14	7/7/14	100%	Complete
Exec. Team Touchpoint Meeting (Provost / VP /	38	1	0.03	10/2/14	10/2/14	100%	Complete
Core Group Planning Meeting #3	39	1	0.03	9/9/14	9/9/14	100%	Complete
Publish Planning Report	40	41	1.37	10/22/14	12/1/14	7%	Future Task
Distribute Planning Report	41	1	0.03	12/4/14	12/4/14	0%	Future Task
University Review / Comment Period	42	11	0.37	12/4/14	12/15/14	0%	Future Task
Document Development	**43**	**1**	**0.03**	**8/18/14**	**8/18/15**	**3%**	**On Schedule**
Schematic Design	44	42	1.4	12/8/14	1/19/15	0%	Future Task
University Review	45	11	0.37	1/19/15	1/29/15	0%	Future Task
Design Development	46	60	2	1/29/15	3/30/15	0%	Future Task
University Review	47	11	0.37	3/30/15	4/10/15	0%	Future Task
CM+R GMP & Approval to Proceed	48	14	0.47	3/25/15	4/8/15	0%	Future Task
Fall Semester 2014	49	117	3.9	8/18/14	12/12/14	50%	On Schedule
Construction Documents Enevolope	50	75	2.5	11/19/14	2/2/15	2%	Future Task
Spring Semester 2015	51	118	3.93	1/12/15	5/9/15	0%	Future Task
BOT Submittal Due	52	2	0.07	2/27/15	3/1/15	0%	Future Task
Borad of Trustees March Meeting	53	1	0.03	3/31/15	3/31/15	0%	Future Task
BOT Submittal Due	54	3	0.1	4/17/15	4/20/15	0%	Future Task
Summer Semester 2015	55	82	2.73	5/18/15	8/7/15	0%	Future Task
Board of Trustees June Meeting	56	1	0.03	5/20/15	5/20/15	0%	Future Task
Bidding Enevlope Scope	57	30	1	4/20/15	5/20/15	0%	Future Task
Enevolope Constrution	58	90	3	5/20/15	8/18/15	0%	Future Task
Construction Documents	59	90	3	4/15/15	7/14/15	0%	Future Task
Bidding Contract Award	60	60	2	6/1/15	7/31/15	0%	Future Task
BOT Submittal Due	61	3	0.1	5/22/15	5/25/15	0%	Future Task
Board of Trustees May Meeting	62	1	0.03	6/24/15	6/24/15	0%	Future Task
Construction Contracts Start	63	1	0.03	7/17/15	7/18/15	0%	Future Task
Fall Semester 2015	64	110	3.67	8/24/15	12/11/15	0%	Future Task
BOT Submittal Due	65	3	0.1	8/21/15	8/24/15	0%	Future Task
Board of Trustees September Meeting ?	66	1	0.03	9/23/15	9/23/15	0%	Future Task

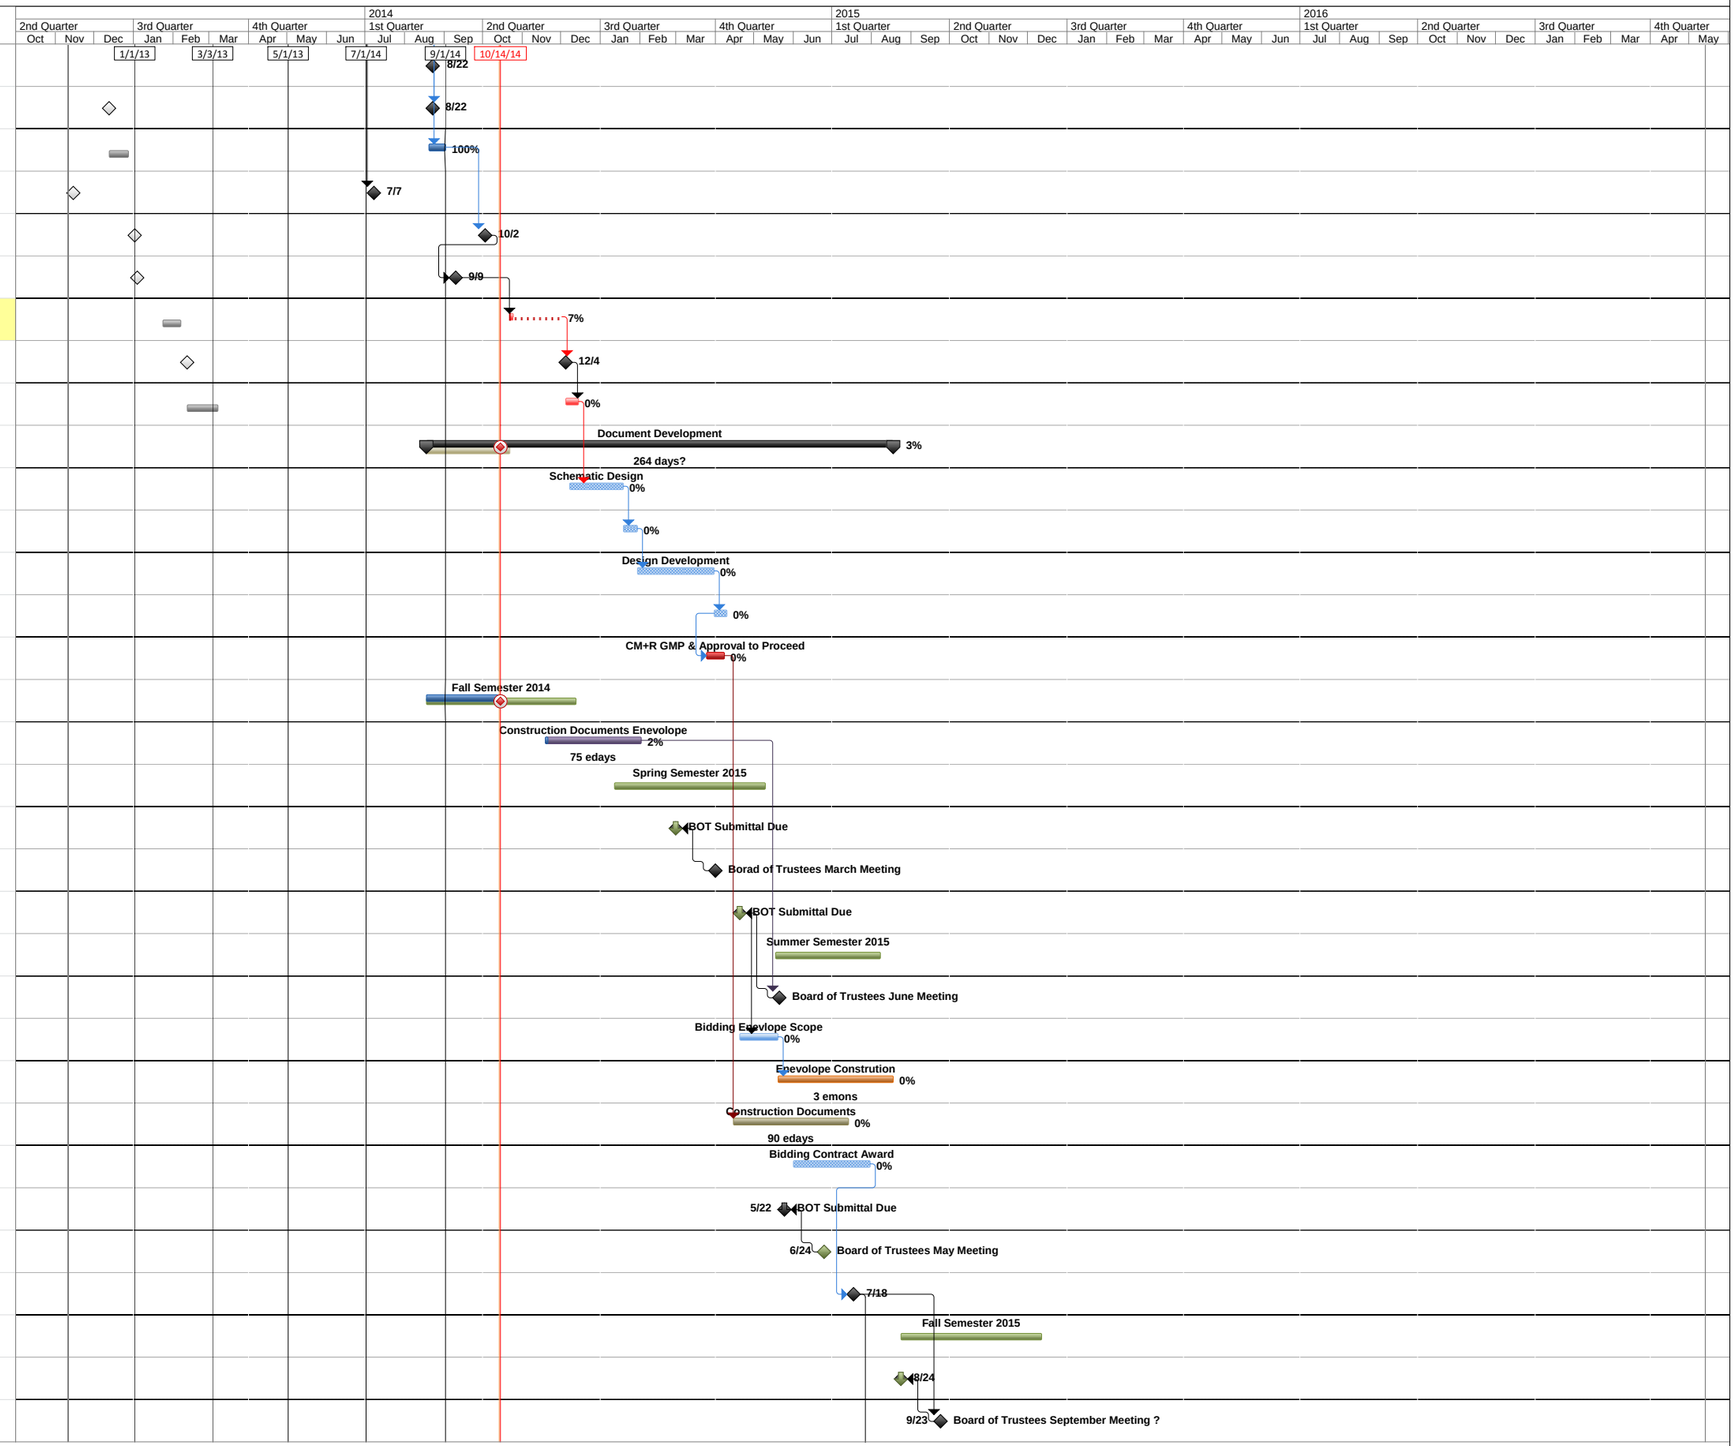

Critical | Task | Manual Task | Duration-only | Baseline Milestone | Summary | External Tasks | Inactive Milestone
Critical Split | Split | Start-only | Baseline | Milestone | Manual Summary | External Milestone | Inactive Summary
Critical Progress | Task Progress | Finish-only | Baseline Split | Summary Progress | Project Summary | Inactive Task | Deadline

Task Name	ID	Calander Days	No. Months	Start	Finish	% Comple	Status
Spring Semester 2016	67	118	3.93	1/18/16	5/14/16	0%	Future Task
Construction	68	365	12.17	7/18/15	7/17/16	0%	Future Task
BOT Submittal Due	69	1	0.03	10/19/15	10/20/15	0%	Future Task
Board of Trustees November Meeting ?	70	1	0.03	11/19/15	11/19/15	0%	Future Task
Summer Semester 2016	71	85	2.83	5/20/16	8/12/16	0%	Future Task
Fall Semester 2016	72	112	3.73	8/29/16	12/18/16	0%	Future Task
A/E & CM+R Contracts Complete	73	90	3	7/17/16	10/15/16	0%	Future Task
Spring Semester 2017	74	118	3.93	1/16/17	5/13/17	0%	Future Task

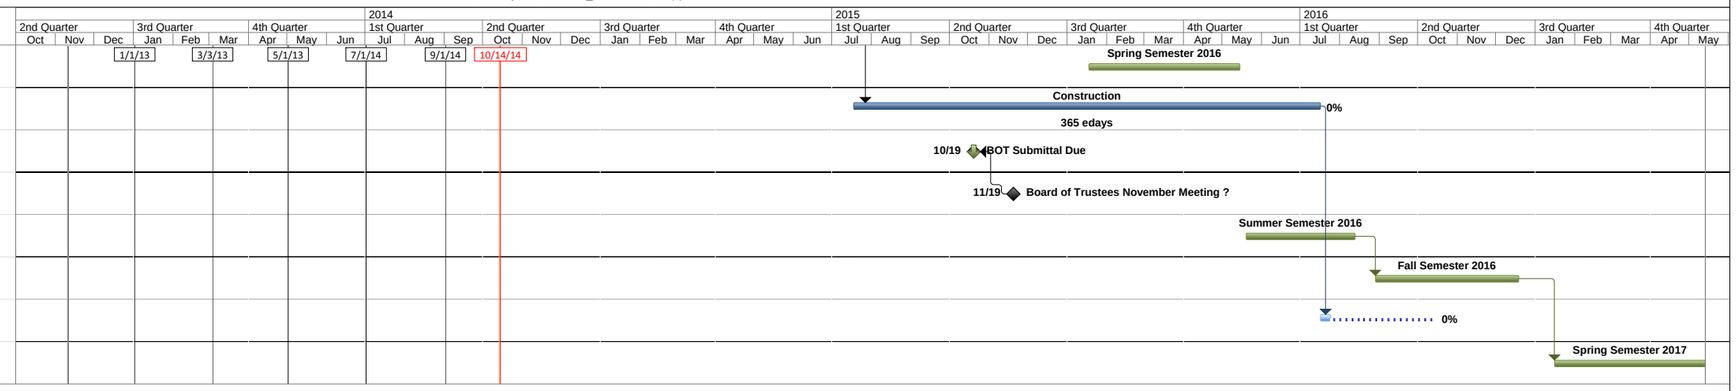

Critical | Task | Manual Task | Duration-only | Baseline Milestone | Summary | External Tasks | Inactive Milestone
Critical Split | Split | Start-only | Baseline | Milestone | Manual Summary | External Milestone | Inactive Summary
Critical Progress | Task Progress | Finish-only | Baseline Split | Summary Progress | Project Summary | Inactive Task | Deadline
